

LEISH.MY · LAUNCH MARKETING PLAN · 90 DAYS

One launch · October 5, 2026 · Three ways to play it

# All Budget Tiers

HIGH

**RM 96,000**

1,500 clients · 25–30 bookings/wk

MEDIUM

**RM 40,000**

800 clients · 15–20 bookings/wk

LOW

**RM 10,000**

300 clients · 6–10 bookings/wk

Full details: [docs/launch-marketing-plan\\*.md](#) · decks: [launch-marketing-plan\\*.pptx](#)

## TIER 1 · HIGH BUDGET

Same launch date · same campaign · scaled execution — see [docs/launch-marketing-plan-tiers.md](#) for the comparison.

*#BookBeautyAnywhere · #NeverDMForADate*

LEISH.MY · LAUNCH MARKETING PLAN · 90 DAYS

Malaysia's beauty booking marketplace — official launch **October 5, 2026**

# Never DM for a Date Again.

**RM 96,000**

TOTAL BUDGET

**clients**

**25–30 bookings/wk · 60+ artists · 1,500**

DAY-90 TARGETS

**Oct 5, 2026**

LAUNCH DATE

Aligned with the FY26 financial forecast — Year-1 revenue RM 180–250k · 20% commission · avg booking RM 250–350

# The Play

WHY

**is broken**  
**Beauty booking in Malaysia**

Leish!'s wedge.  
owns real-time MUA booking — that's  
ghosting and late payments. Nobody  
quote. Artists drown in DM chaos,  
Clients DM 15 artists and wait days for a

**Launch theme: Never DM for a date again**

WHAT

**A two-sided marketplace**

reminders and payouts.  
Artists get portfolios, bookings,  
confirmation and secure Billplz payment.  
studios with real-time availability, instant  
Clients book vetted makeup artists &

**Artist theme: Get booked. Get paid.**

HOW

**Both sides, supply first**

Launch at the peak of wedding season.  
through paid, KOLs, events and PR.  
(critical path), then drive client demand  
Recruit 30 anchor artists before Day 0

**Hero categories: Bridal · Hijab · Event**

# Two messages, one marketplace

TO CLIENTS

confirmation, secure payment.”  
minutes — real-time availability, instant  
“Book Malaysia's top makeup artists & studios in

TO ARTISTS & STUDIOS

payments.”  
zero admin — we handle bookings, reminders and  
“Get booked. Get paid. Your portfolio, your pricing,

WHAT THE PLATFORM ALREADY HAS — USE IT

Instant booking + Billplz payments

Real-time availability & reviews

Artist/studio profiles with portfolios

Rewards + Leish+ (RM29/mo) upsell

WhatsApp booking flow


Brevo email (hello@leish.my)

GA4 + Meta Pixel installed

Artist shareable profile links

TIMELINE

# Four phases, one launch

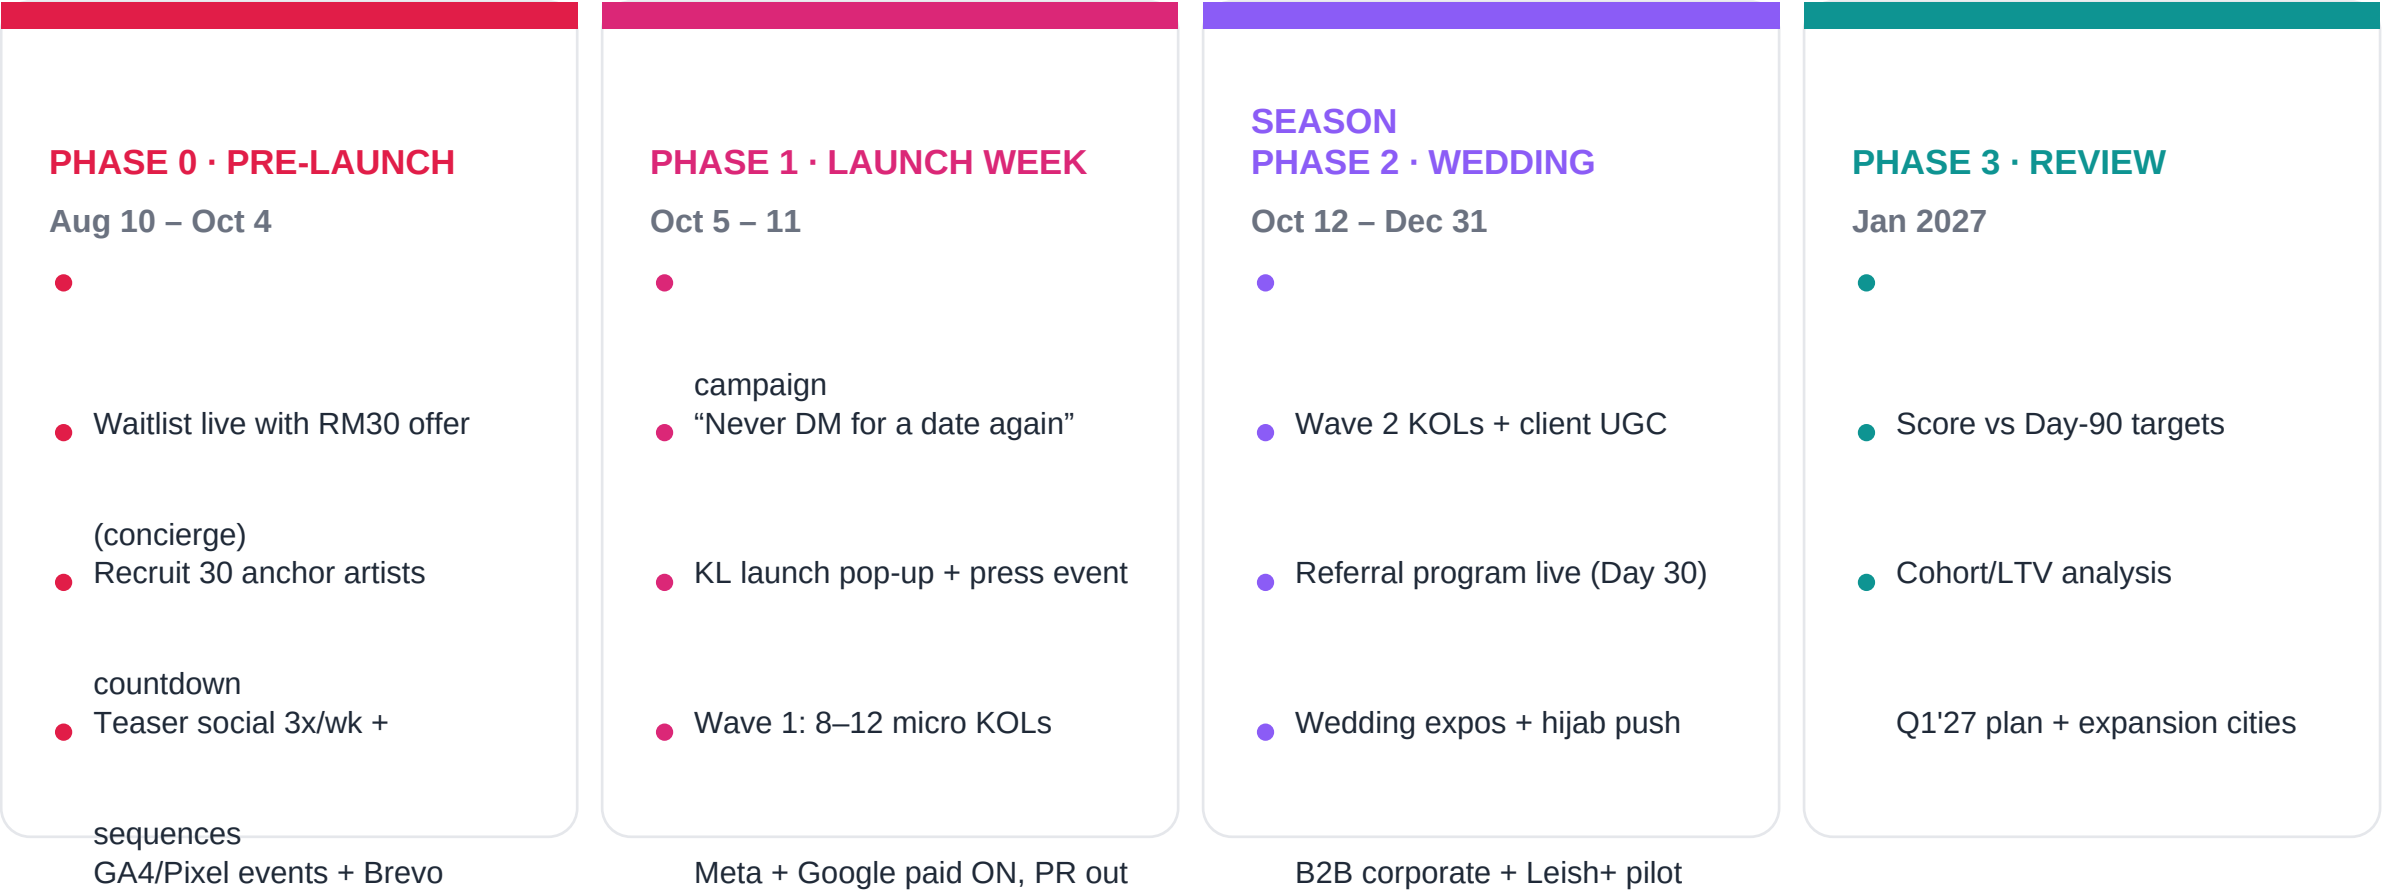

# Day-90 Targets

1,500

Registered clients

60+

Active artists & studios

25–30

Bookings / week

RM 7–9k

GMV / week

≤ RM 20

Client CAC (paid)


2.5–3.5x

Blended ROAS

| KPI                           | Pre-launch     | Day 30 | Day 60   | Day 90         |
|-------------------------------|----------------|--------|----------|----------------|
| Waitlist / clients            | 2,000 waitlist | 600    | 1,000    | 1,500          |
| Weekly bookings               | —              | 12     | 20       | 25–30          |
| Commission revenue / wk (20%) | —              | RM 700 | RM 1,200 | RM 1,500–1,800 |
| Email list                    | 2,500          | 4,000  | 5,000    | 6,000          |
| Social following              | 3,000          | 6,000  | 8,000    | 10,000         |

RM 96,000 · 90 DAYS

# Budget Breakdown

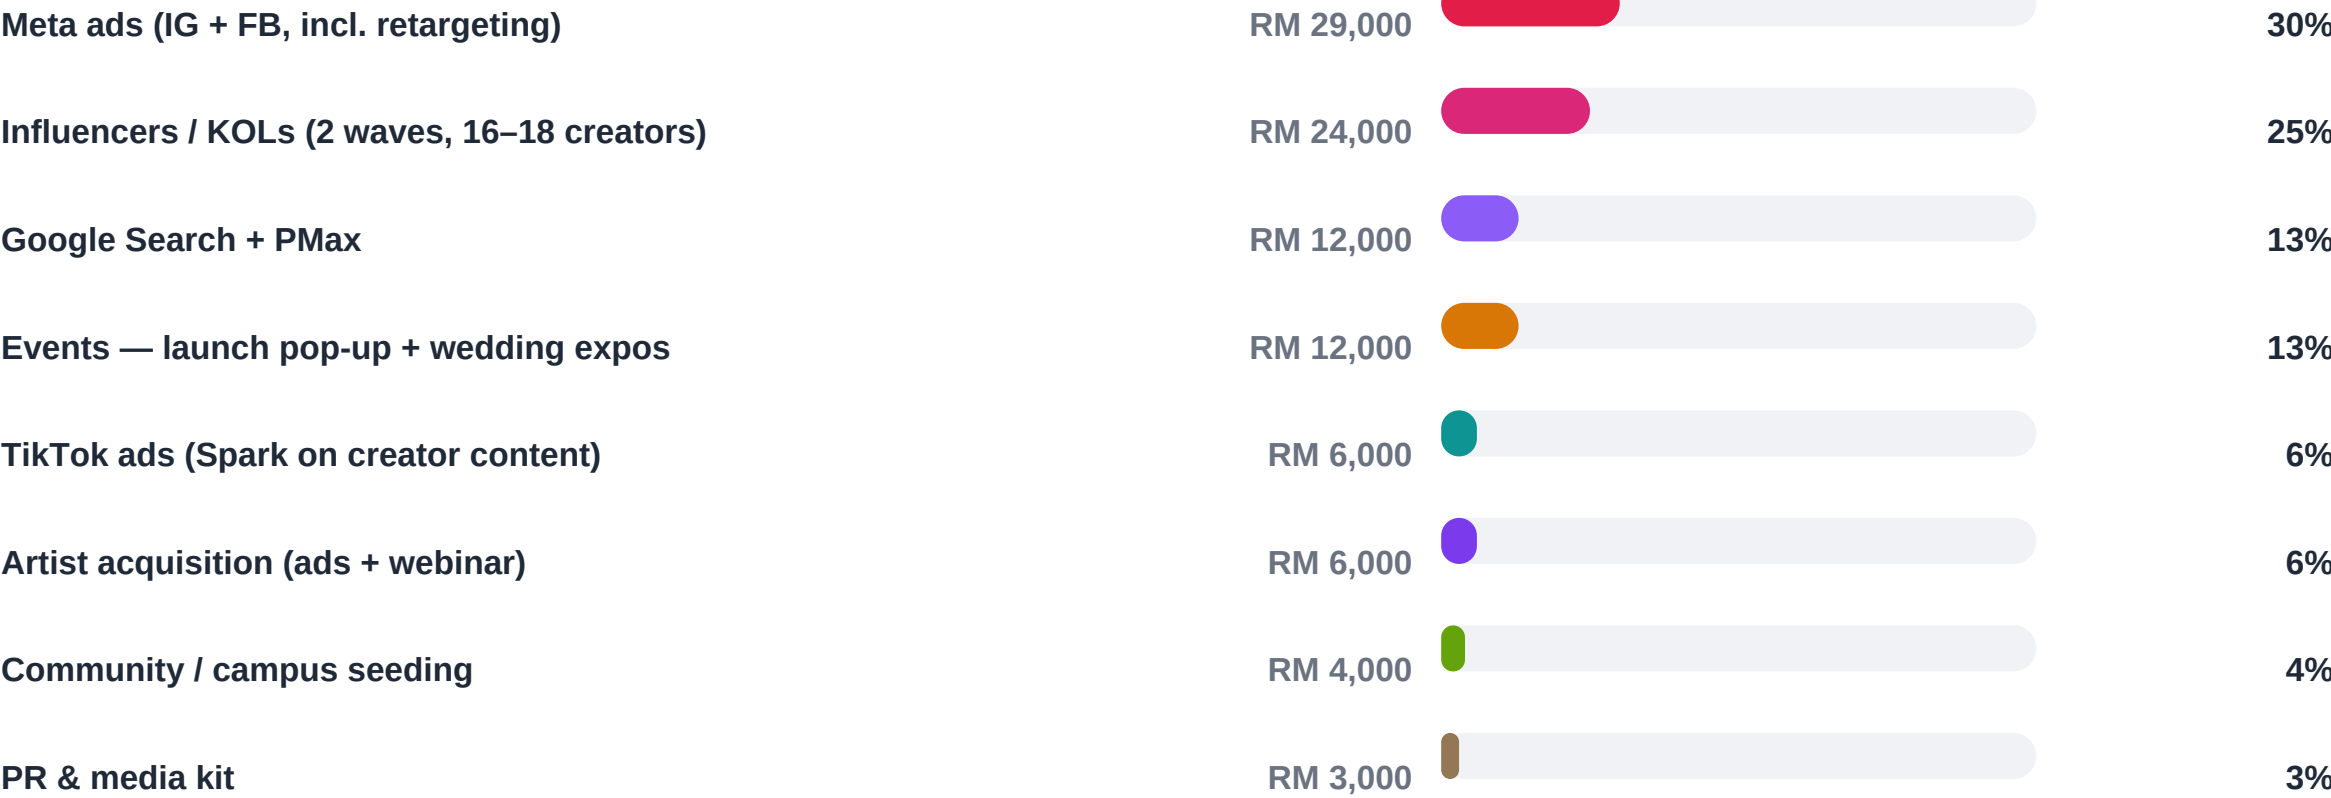

this is a growth test, not a burn.  
**Payback logic:** blended CAC RM20 → client LTV RM 90–150 (2–3 bookings × RM 300 × 20%). CAC pays back in 1–2 bookings. Kill or scale by ROAS weekly —



# Owned · Paid · Earned

## OWNED — foundation

- Instagram — 4–5 posts + 10 stories + 2 reels / wk
- TikTok — 3–4 UGC-style reels / wk
- Facebook + bridal/beauty groups — daily participation
- Email (Brevo) — lifecycle sequences + 2 newsletters/mo
- WhatsApp API — confirmations, reminders, broadcasts
- SEO — 2 blogs/mo on /inspiration + /events

## PAID — RM 47k

- Meta (IG+FB) RM 24k — bridal/beauty interest stacks, KL-Selangor, 20–40
- Google RM 12k — high-intent: “bridal makeup KL”, “MUA near me”
- TikTok RM 6k — Spark Ads on creator content
- Retargeting RM 5k — visitors, waitlist & cart abandoners, RM30 creative
- Artist-side ads — target working MUAs (“switch from DM chaos”)

## 43k EARNED + COMMUNITY — RM

- 2 KOL waves — 16–18 micro/mid creators, flat + booking-code commission
- 1–2 wedding expos + KL launch pop-up (glam bar)
- wedding blogs
- PR — SAYS, The Star, Malay Mail, NST,
- Giveaways in bridal FB groups
- Limkokwing, UPM area)
- Campus pop-ups — Cyberjaya (MMU,
- Free “grow your MUA business” webinar (Nov)

LOCK BEFORE DAY 0

# Launch Offers & Promotions

## CLIENT SIDE (DEMAND)

### LEISH30

RM30 off first booking · cap 300 · valid to Day 30

### Early-bird bonus

Waitlist members get RM30 + priority access

### Refer-a-friend

RM20 credit each · live from Day 30

## ARTIST SIDE (SUPPLY)

### Free 3-month Pro listing

Normally RM 200–500/mo · cap 50 artists

### 0% commission, first 10 bookings

vs standard 20% · cap 30 artists

### Artist referral

RM100 + featured slot when referee hits 5 bookings

■ **Pre-launch dev task:** verify promo-code / credit support in admin. If unsupported, use UTM + support-issued credits and log a dev task before Aug 24.

# Content Calendar — Highlights

| Week        | Theme             | Hero content                                | Campaign           |
|-------------|-------------------|---------------------------------------------|--------------------|
| W1 · Aug 10 | Tease             | Founder story reel — “Why we built Leish!”  | Waitlist open      |
| W2          | Artist spotlight  | “Meet the artist” carousels ×3              | Artist recruitment |
| W3          | Pain-point comedy | “POV: DM-ing 15 MUAs for your wedding date” | Waitlist           |
| W4          | Education         | Bridal makeup cost guide KL 2026            | Waitlist           |
| W5          | Proof             | Beta client before/after + testimonial      | Waitlist           |
| W6          | Countdown         | “Leish! launches Oct 5” series              | Launch hype        |
| W7 · Oct 5  | LAUNCH WEEK       | Event content, KOL posts, LEISH30 code      | DAY 0              |
| W8          | Social proof      | UGC roundup + first bookings                | Post-launch        |
| W9          | Hijab series      | Hijab MUA directory + looks                 | Community          |
| W10         | Wedding season    | “Book your wedding MUA now” urgency         | Paid push          |
| W11         | Referrals         | Refer-a-friend launch creative              | Referral           |
| W12         | Festive prep      | CNY / Raya early-bird booking               | Festive            |

Weddings” · “10 Questions to Ask Your MUA”  
**Evergreen SEO (2/mo):** “Best Bridal Makeup Artists in KL & Selangor 2026” · “How Much Does Bridal Makeup Cost in Malaysia?” · “Hijab Makeup Looks for

# Risks & Mitigations

| Risk                               | L    | I    | Mitigation                                                                                                                                                 |
|------------------------------------|------|------|------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Not enough artists at launch       | Med  | High | Concierge recruitment from T-6; 30-artist gate — delay Day 0 if short                                                                                      |
| Demand lags supply (artists churn) | Med  | High | Weekly zero-booking check; demand ads + featured rotation; commission-free period                                                                          |
| Checkout friction (Billplz)        | Med  | High | Track booking_started→completed; A/B deposit vs full payment; WhatsApp assist                                                                              |
| KOL underperformance               | Med  | Med  | 60/40 flat + booking commission; test 4 in wave 1 before wave-2 spend                                                                                      |
| Promo abuse (RM30 codes)           | Med  | Low  | One code per account; cap 300; fraud flag on repeat emails                                                                                                 |
| SEO ramp too slow                  | High | Low  | Content engine from Day 1; treat SEO as 6-month play; rely on paid + social at launch                                                                      |
| Traffic spike / infra              | Low  | High | Launch-ready  ; load-test /artists + /bookings; UPSTASH Redis in prod |

**Guardrails:** artists idle 14+ days · no-show/cancellation <15% · artist response <4 hrs · search→booking ≥2%

# Owner Matrix

|        |                                              |        |                                                     |
|--------|----------------------------------------------|--------|-----------------------------------------------------|
| Aug 10 | Confirm launch date + sign-off on plan       | Sep 21 | Launch pop-up venue + invite list                   |
| Aug 17 | Hire/assign marketing lead + content creator | Sep 28 | 30 anchor artists recruited (gate!)                 |
| Aug 24 | Waitlist page live + RM30 offer configured   | Sep 28 | Paid campaigns live (test) → full Oct 5             |
| Aug 24 | GA4 + Meta events verified (10 events)       | Oct 5  | DAY 0 — official launch                             |
| Aug 31 | Brevo sequences + UTM scheme live            | Nov 4  | Referral live · wedding expo booked · Day-30 review |
| Sep 21 | Media kit + press release drafted            | Dec 4  | Leish+ pilot to top clients                         |
| Sep 21 | KOL wave 1 contracted (8–12)                 | Jan 4  | Day-90 review + Q1'27 plan                          |

CLOSE BY AUG 10

# Open Questions for the Founder

1

## **Confirm launch date**

Oct 5, 2026 proposed — first Monday after Hari Malaysia week, peak wedding season.

2

## **Budget sign-off**

RM 96,000 / 90 days, drawn from seed runway per financial forecast.

3

## **Promo-code system**

Does admin support codes/credits, or is a dev task needed before Aug 24?

4

## **Marketing owner**

In-house hire vs agency vs founder-led with this plan as the ops doc — #1 dependency.

5

## **Brand assets**

IG/TikTok/FB handles (@leish.my?), logo kit, press photos.

6

## **Leish+ timing**

Keep RM29/mo pilot internal for 90 days; public in Q1'27 (recommended).

7

## **Legal & compliance**

PDPA consent on waitlist capture + contest T&Cs before any giveaway.

WEEKLY DASHBOARD, EVERY MONDAY

# Measurement & Attribution

## EVENTS TO VERIFY (GA4 + META)

- waitlist\_signup
- sign\_up
- search
- view\_artist
- booking\_started
- booking\_completed (value = booking value)
- payment\_success
- artist\_application\_started
- share\_link\_clicked

## WEEKLY DASHBOARD SECTIONS

- 
- Growth — waitlist, signups, artists, bookings, GMV, commission
- Funnel — search → artist view → booking\_start → complete
- Paid — spend, ROAS, CAC, CPM/CPC by channel
- Quality — no-show, cancellation, avg rating, repeat rate
- Content — email list, opens/clicks, reach, top posts

## ATTRIBUTION

channel.

UTM on every outbound link — source / medium / campaign / term / content (scheme in plan Appendix C). Capture source at signup. Report: bookings & CAC by —

# Ready to glow.

Full plan: [docs/launch-marketing-plan.md](#) · Summary: [docs/launch-marketing-plan-summary.md](#)

**Next step:** close the 7 blockers by Aug 10, then execute the 30-day checklist.

*#BookBeautyAnywhere · #NeverDMForADate · Your Beauty, Perfected.*



## TIER 2 · MEDIUM BUDGET

Same launch date · same campaign · scaled execution — see [docs/launch-marketing-plan-tiers.md](#) for the comparison.

*#BookBeautyAnywhere · #NeverDMForADate*

LEISH.MY · LAUNCH MARKETING PLAN · 90 DAYS

Never DM for a Date Again. — official launch **October 5, 2026**

# Medium Budget

**RM 40,000**

TOTAL BUDGET

**bookings/wk**

**800 clients · 40–45 artists · 15–20**

DAY-90 HEADLINE

**Oct 5, 2026**

LAUNCH DATE

wedding-season timing.

Founder + one part-time marketer. Co-hosted pop-up launch, one micro-KOL wave, Meta + narrow Google. Lean execution, same

# The Play — Medium Budget

FOCUS

**Lean paid, high intent**

weeks.  
Every ad set gated at 2x ROAS after 2 Retargeting gets 20% of Meta budget. top-10 keywords). No TikTok ads. Meta RM 12k + Google RM 4k (brand +

STYLE

**Co-hosted pop-up launch**

lead-cost projection by Sep 15.  
wedding expo OR pop-up — decide by brings booking tech + offers. One Partner studios host the venue; Leish!

GROWTH LOOP


**Commission-heavy KOLs**

then referral program from Day 30. GMV) so they self-motivate. One wave, 50% booking-code commission (10% of 6–8 micro creators (10k–50k), 50% flat /

Artist gate before Day 0: 25 bookable artists by Sep 28 · Campaign: Never DM for a date again · Hero categories: Bridal · Hijab · Event

RM 40,000 · 90 DAYS

# Budget Breakdown

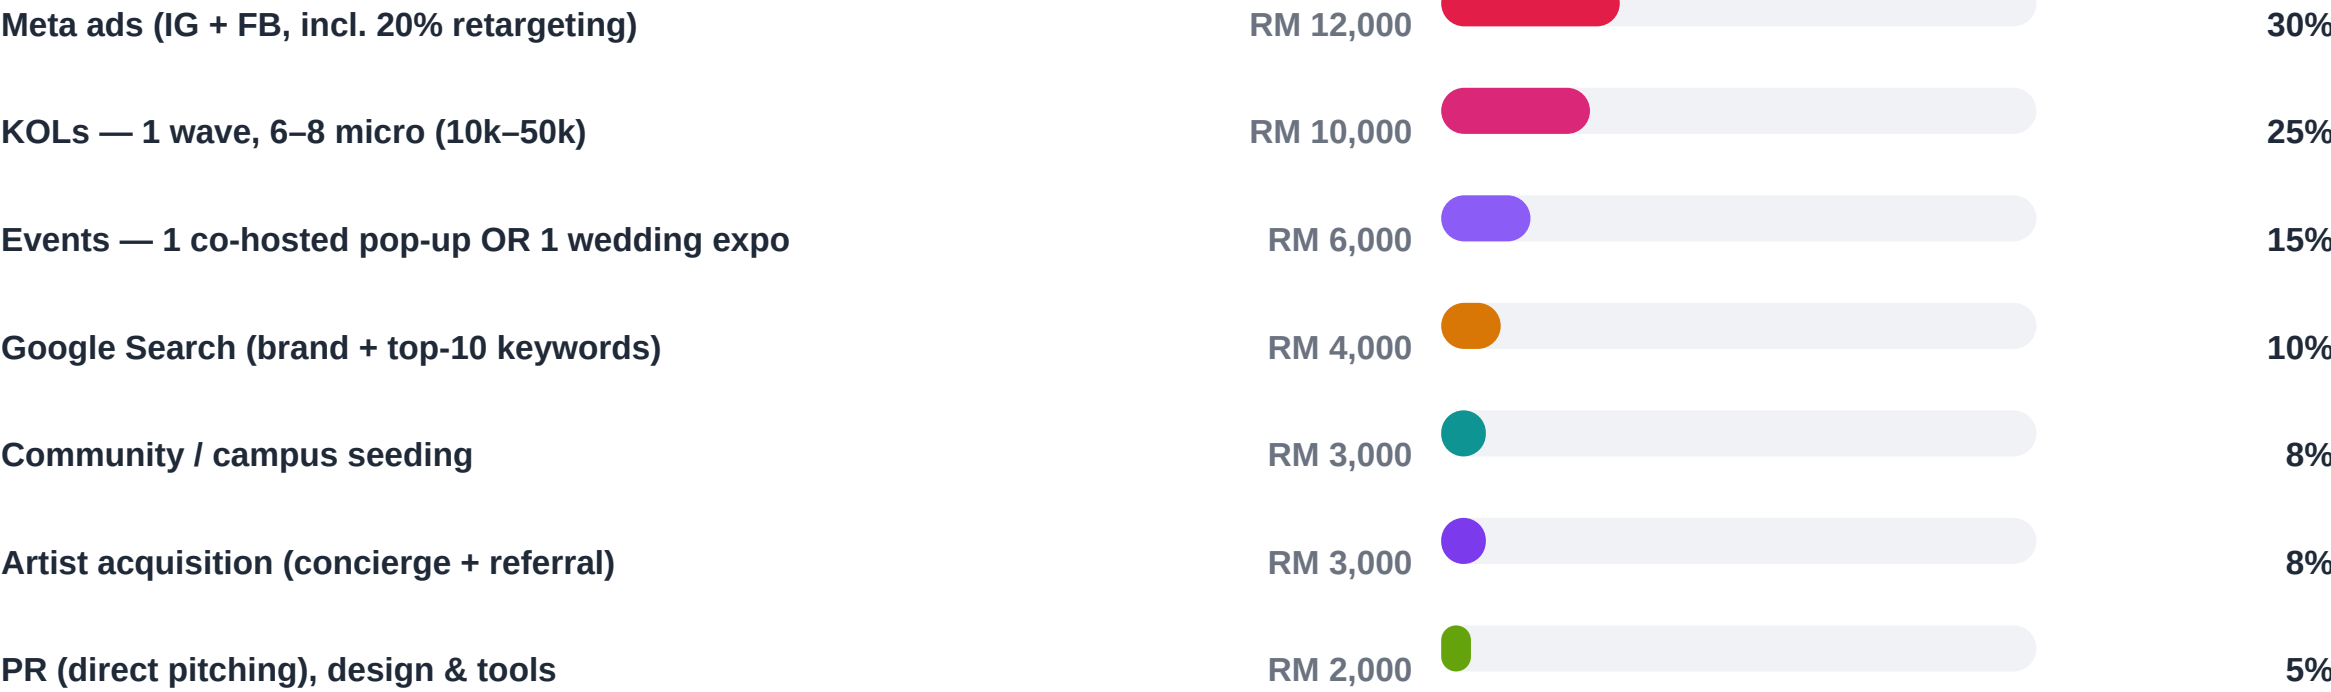

**Payback logic:**  $CAC \leq RM\ 25 \rightarrow$  client LTV RM 90–150 (2–3 bookings  $\times$  RM 300  $\times$  20%). Payback in 1–2 bookings; ROAS gate  $\geq 2.5x$ .

# Day-90 Targets

800

Registered clients

40–45

Active artists & studios

15–20

Bookings / week

RM 4.5–6k

GMV / week

≤ RM 25

Client CAC (paid)

≥ 2.5x

Blended ROAS

PROGRESSION

| KPI                   | Pre-launch     | Day 30 | Day 60 | Day 90       |
|-----------------------|----------------|--------|--------|--------------|
| Waitlist / clients    | 1,000 waitlist | 300    | 550    | 800          |
| Weekly bookings       | —              | 6–8    | 12     | 15–20        |
| Commission / wk (20%) | —              | RM 400 | RM 700 | RM 900–1,200 |
| Email list            | 1,500          | 2,000  | 2,500  | 3,000        |
| Social following      | 1,500          | 2,500  | 3,800  | 5,000        |

TIMELINE

Four phases

|                                                                                                                                                                                                                                                                                                    |                                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                           |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><div>PHASE 0 · PRE-LAUNCH</div><div>Aug 10 – Oct 4</div><div><div></div><div>● Green-light Aug 10</div><div>● Waitlist live Aug 31 (RM30 offer)</div><div>● 25 anchor artists, concierge</div></div></div> <div><div>● Teaser content 2x/wk</div><div>● KOLs contracted by Sep 31</div></div> | <div><div>PHASE 1 · LAUNCH WEEK</div><div>Oct 5 – 11</div><div><div></div><div>studios</div><div>● Co-hosted pop-up with partner</div><div>● 6–8 micro KOLs post</div><div>● Direct-journalist PR pitch</div></div></div> <div><div>● Meta + Google full ON</div><div>● LEISH20 live</div></div> | <div><div>PHASE 2 · WEDDING SEASON</div><div>Oct 12 – Dec 31</div><div><div></div><div>(RM15/RM15)</div><div>● Referral program Day 30</div><div>pop-ups</div><div>● 1 expo booth OR 2 campus</div><div>● Hijab community push (Nov)</div></div></div> <div><div>● B2B light — 2–3 pitches</div><div>● 1 blog/mo SEO</div></div> | <div><div>PHASE 3 · REVIEW</div><div>Jan 2027</div><div><div></div><div>● Score vs Day-90 targets</div><div>→</div><div>● ≥12 bookings/wk + CAC ≤ RM 25</div><div>● upgrade to High for CNY</div></div></div> <div><div>else fix or downgrade</div></div> |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

# Owned · Paid · Earned

## OWNED — FOUNDATION

- 
- IG — 3–4 posts + 7 stories + 1 reel / wk
- TikTok — 2 reels / wk (repurposed)
- FB + bridal/beauty groups — daily
- Email (Brevo) — sequence + 1 newsletter/mo
- WhatsApp — confirmations + monthly broadcast
- SEO — 1 blog/mo on /inspiration + /events

## PAID — RM 16K

- 
- KL-Selangor, 20–40
- Meta RM 12k — bridal/beauty stacks,
- Retargeting = 20% of Meta budget
- keywords
- Google RM 4k — brand + top-10 high-intent
- No TikTok ads at this tier
- Kill any ad set <2x ROAS after 2 weeks

## 19K EARNED + COMMUNITY — RM

- 
- commission
- 6–8 micro KOLs — 50/50 flat + booking
- 1 co-hosted pop-up OR 1 wedding expo
- Limkokwing)
- 2 campus pop-ups — Cyberjaya (MMU,
- Direct PR pitch — SAYS, The Star, Malay Mail
- Bridal FB group giveaways (RM 500)

LOCK BEFORE DAY 0

# Launch Offers & Promotions

## CLIENT SIDE (DEMAND)

### LEISH30

RM30 off first booking · cap 150 · valid to Day 30

### Early-bird bonus

Waitlist members get RM30 + priority access

### Refer-a-friend

RM15 credit each · live from Day 30

## ARTIST SIDE (SUPPLY)

### Free 3-month Pro listing

Normally RM 200–500/mo · cap 30 artists

### 0% commission, first 10 bookings

vs standard 20% · cap 20 artists

### Artist referral

RM100 + featured slot on referee's 5th booking

■ Pre-launch dev task: verify promo-code / credit support in admin before Aug 24 (same as High tier).



# Risks & Mitigations

Small team = content slippage

Batch content weekly (2 blocks/wk); templates; outsource design per-asset.

Only 1 KOL wave

Commission-heavy 50/50 deals; secure 2-month UGC rights in contracts.

Thin paid budget

Kill <2x ROAS ad sets after 2 weeks; 20% of Meta budget to retargeting.

Artist gate not met (25)

Start concierge Aug 31; fallback: extend free Pro to 6 months.

artists idle 14+ days · no-show <15% · artist response <4 hrs · search→booking ≥2%  
Pop-up vs expo choice

Decide by lead-cost projection; book by Sep 15.

# Execute · Measure · Decide

## 30-DAY CHECKLIST

|        |                            |
|--------|----------------------------|
| Aug 10 | Confirm date + budget      |
| Aug 24 | Part-time marketer hired   |
| Aug 31 | Waitlist + RM30 offer live |
| Sep 21 | KOL wave contracted (6–8)  |
| Sep 28 | 25 anchor artists (gate!)  |
| Oct 5  | DAY 0 — launch             |

by Sep 15.  
GA4/Meta events verified Aug 31 · paid test Sep 28 → full Oct 5 · pop-up/expo locked

## UPGRADE / DOWNGRADE

|           |                                                                                                                                                 |
|-----------|-------------------------------------------------------------------------------------------------------------------------------------------------|
| Upgrade   | 80% → scale to High (RM 96k) for CNY season.<br>Day-60: $\geq 12$ bookings/wk + $CAC \leq RM\ 25$ + artist retention $\geq$ community channels. |
| Downgrade | Day-30: paid $CAC > RM\ 35$ → cut Google + half of Meta; shift to                                                                               |

## REMAINING CHECKLIST

|       |                                      |
|-------|--------------------------------------|
| Nov 4 | Referral live · Day-30 review        |
| Dec 4 | Day-60 checkpoint → upgrade decision |
| Jan 4 | Day-90 review + Q1'27 plan           |

# Growth, with discipline.

Full plan: [docs/launch-marketing-plan-medium.md](#) · Tiers: [docs/launch-marketing-plan-tiers.md](#)

**Next step:** close the 5 tier risks and execute the 12-item checklist; Day-60 checkpoint decides upgrade to High.

*#BookBeautyAnywhere · #NeverDMForADate · Your Beauty, Perfected.*

### TIER 3 · LOW BUDGET

Same launch date · same campaign · scaled execution — see [docs/launch-marketing-plan-tiers.md](#) for the comparison.

*#BookBeautyAnywhere · #NeverDMForADate*

LEISH.MY · LAUNCH MARKETING PLAN · 90 DAYS

Never DM for a Date Again. — official launch **October 5, 2026**

# Low Budget (Bootstrap)

**RM 10,000**

TOTAL BUDGET

**bookings/wk**

**300 clients · 25 artists · 6–10**

DAY-90 HEADLINE

**Oct 5, 2026**

LAUNCH DATE

scale.

Founder-led quiet launch. Community, artist network, referrals and barter — near-zero paid. The goal is proof of unit economics, not

# The Play — Low Budget (Bootstrap)

FOCUS

**Proof, not scale**

Q1'27 CNY season.  
unlock the Medium plan (RM 40k) for  
RM 15 and artist retention  $\geq 80\%$  →  
Hit consistent weekly bookings at CAC  $\leq$

STYLE

**Quiet soft launch**

co-hosted pop-up.  
Growth via bridal FB groups, campus and  
organic posts + LEISH30 on Oct 5.  
No event, no paid splash: waitlist email +

GROWTH LOOP


**People over ads**

— no prospecting.  
UGC contests. RM 2.5k retargeting only  
referral from Day 1, nano-KOL barter,  
Artist share links (built into the product),

Artist gate: 20 bookable artists by Sep 28 · Offers: LEISH30 cap 100 · Free 6-month Pro for artists (compensates for lower traffic)

RM 10,000 · 90 DAYS

# Budget Breakdown

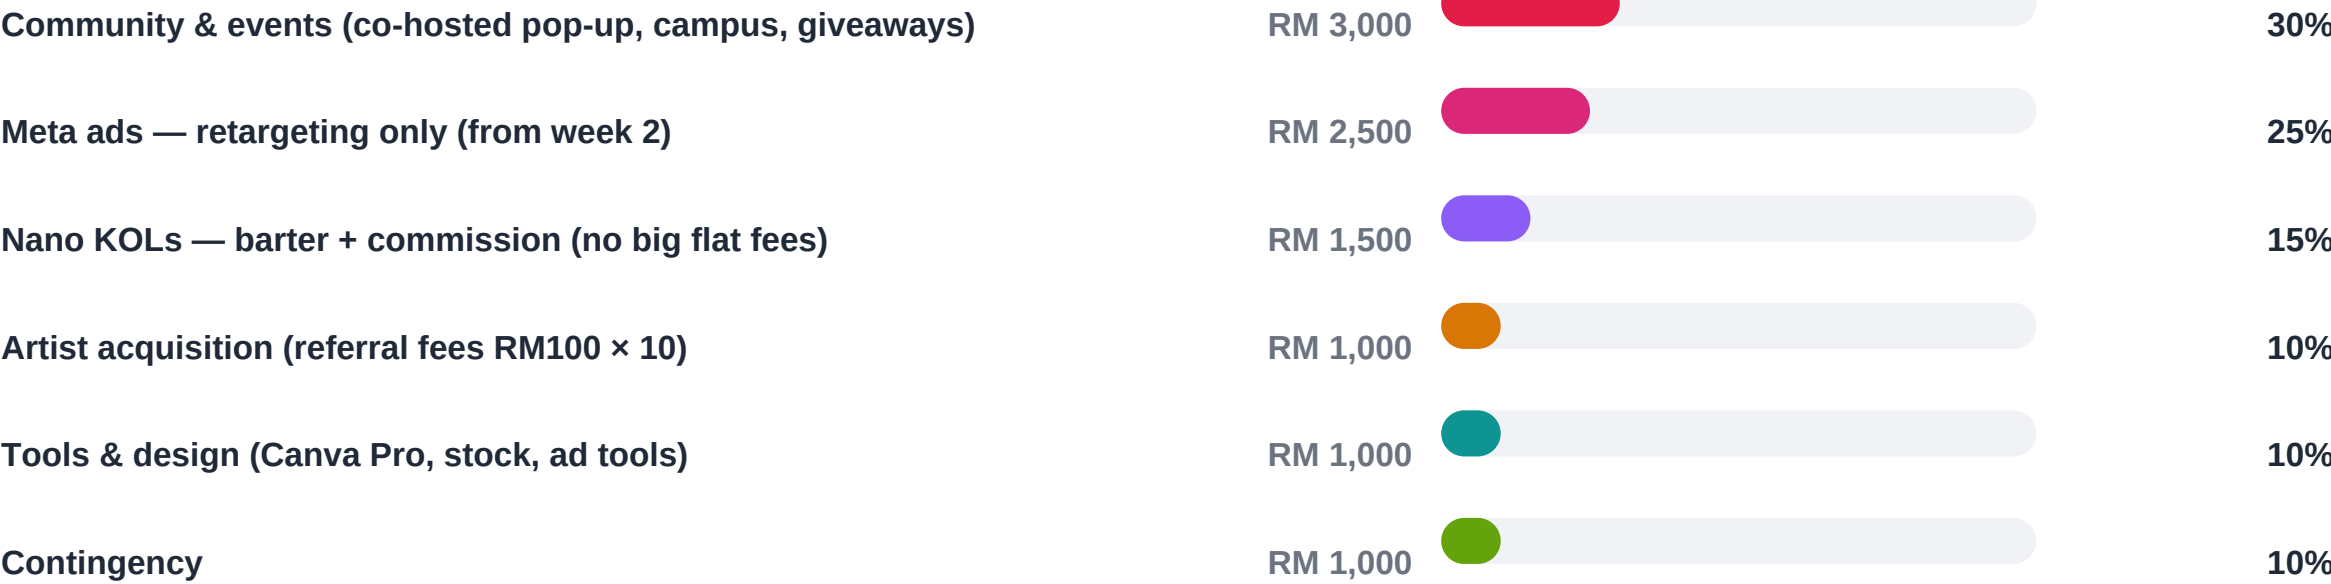

**Payback logic:** Organic-heavy CAC ≤ RM 15 → LTV RM 90–150 = 6–10x LTV:CAC. Paid is retargeting-only (closing), never prospecting, at this scale.

# Day-90 Targets

300

Registered clients

25

Active artists & studios

6–10

Bookings / week

RM 1.8–3k

GMV / week

≤ RM 15

Blended CAC (organic-heavy)

1,200


Email list

PROGRESSION

| KPI                   | Pre-launch   | Day 30 | Day 60 | Day 90     |
|-----------------------|--------------|--------|--------|------------|
| Waitlist / clients    | 400 waitlist | 120    | 220    | 300        |
| Weekly bookings       | —            | 3–4    | 5–7    | 6–10       |
| Commission / wk (20%) | —            | RM 180 | RM 300 | RM 360–600 |
| Email list            | 600          | 800    | 1,000  | 1,200      |
| Social following      | 600          | 1,200  | 1,800  | 2,500      |



# Four phases

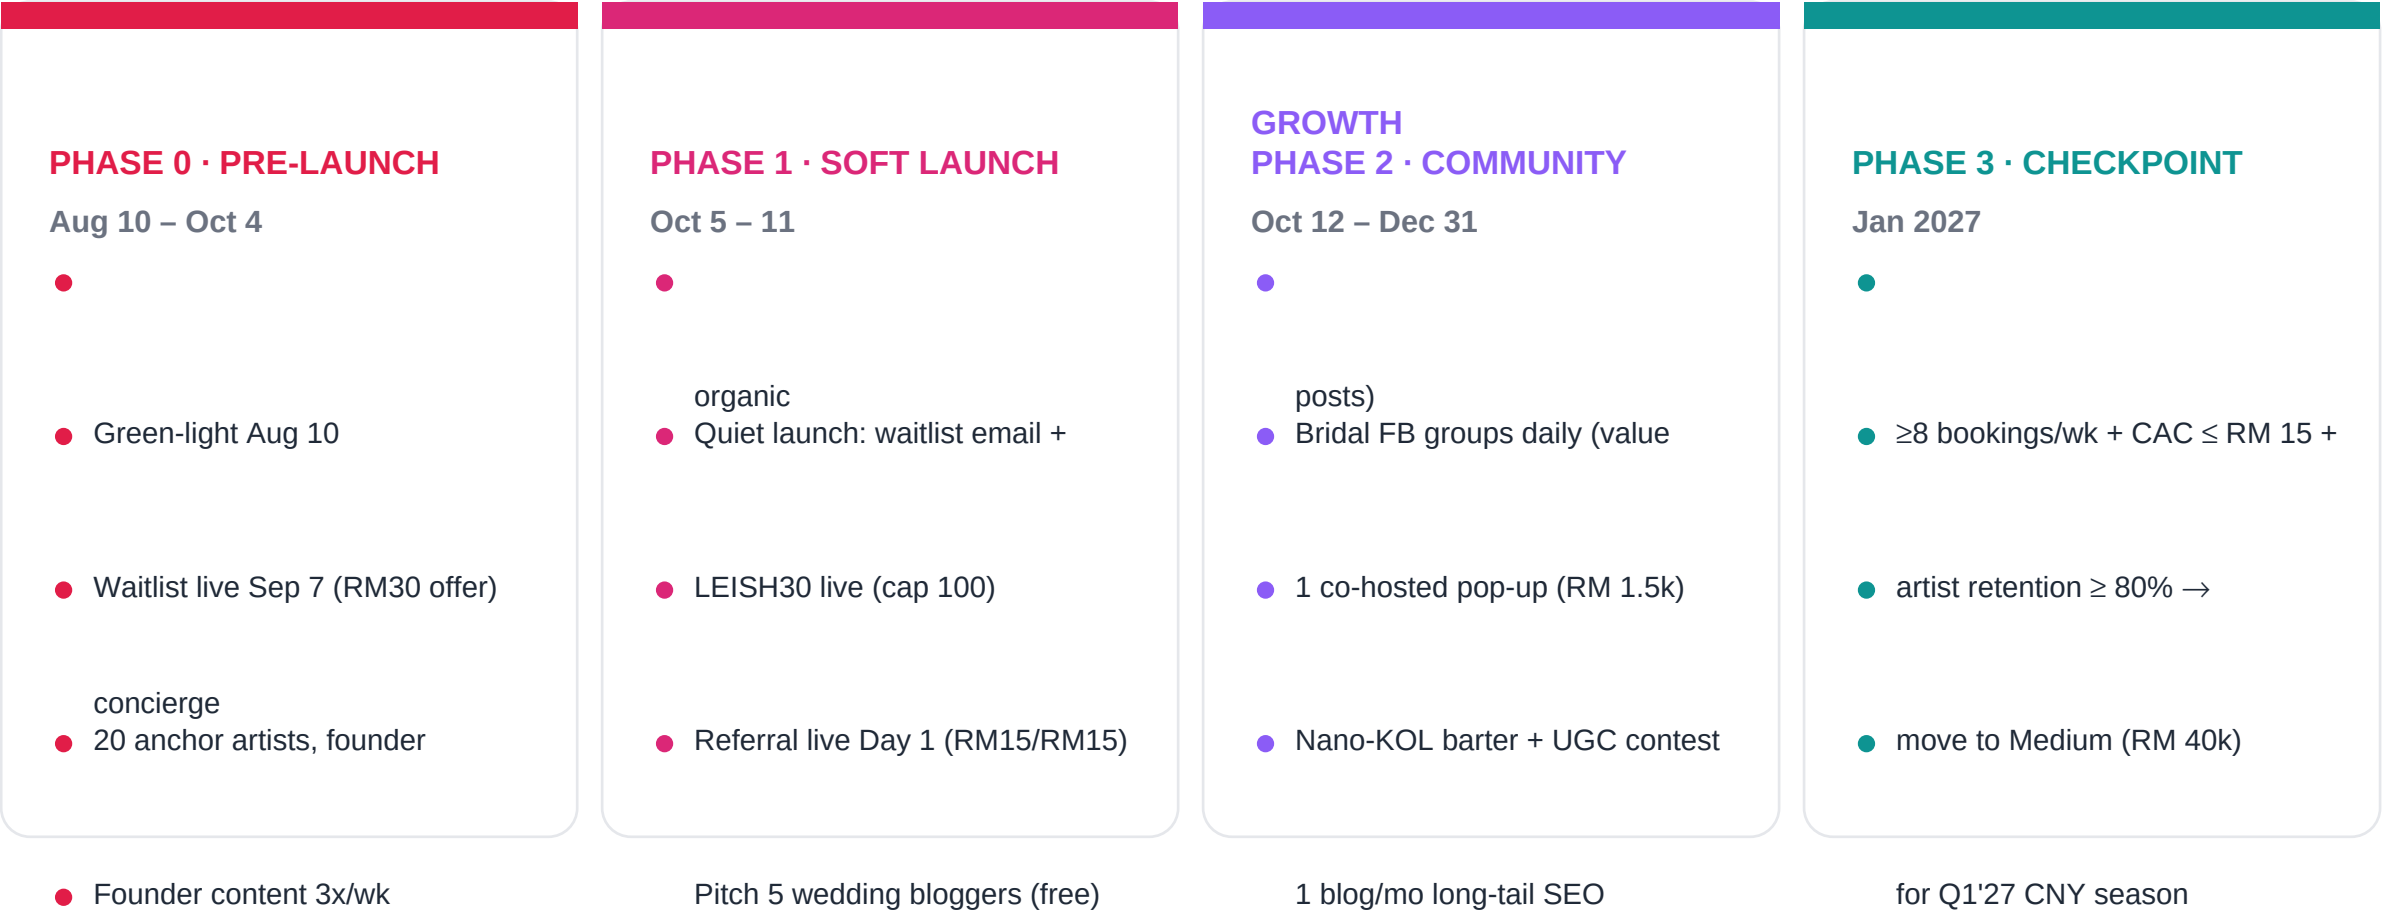

# Owned · Paid · Earned

**WORK**  
**OWNED FIRST — ~85% OF THE**

- 
- IG — 3 posts + daily stories + 1 reel / wk
- TikTok — 1–2 founder reels / wk
- FB + bridal/beauty groups — daily, value-first
- Email (Brevo) — sequence + 1 newsletter/mo
- Artist share links — the #1 acquisition loop
- Founder LinkedIn — weekly build-in-public posts

SEO — 1 long-tail blog/mo

**PAID — RM 2.5K**

- 
- Meta retargeting only, from week 2
- Audiences: site visitors + waitlist abandoners
- Creative: RM30 offer
- No Google · No TikTok ads · No prospecting
- Pause <1.5x ROAS after 2 weeks

**5.5K**  
**EARNED + COMMUNITY — RM**

- 
- Nano KOLs (2k–20k) — barter + 10–15% of GMV
- Ambassador program — top 10 clients, RM50/mo
- 1 co-hosted pop-up with partner studio
- 1 campus pop-up (Cyberjaya)
- Bridal FB group giveaways (RM 500)
- UGC contest — 5 × RM50 vouchers monthly

LOCK BEFORE DAY 0

# Launch Offers & Promotions

## CLIENT SIDE (DEMAND)

### LEISH30

RM30 off first booking · cap 100 · valid to Day 30

### Refer-a-friend

RM15 credit each · live from Day 1

### UGC contest

5 × RM50 vouchers · monthly

## ARTIST SIDE (SUPPLY)

### Free 6-month Pro listing

Normally RM 200–500/mo · cap 25 artists

### 0% commission, first 10 bookings

vs standard 20% · cap 15 artists

### Artist referral

RM100 on referee's 5th booking · cap 10

■ Pre-launch dev task: verify promo-code / credit support in admin before Sep 7 (same as other tiers).

# Risks & Mitigations

|                                                                                                              |                                                                                                 |
|--------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------|
| Demand too slow → artists churn                                                                              | Free 6-month Pro; celebrate every booking publicly; weekly artist check-ins.                    |
| Founder bandwidth                                                                                            | 2 batch content days/wk; templates; hire part-time helper from contingency if bookings justify. |
| No PR / low visibility                                                                                       | FB groups + campus + barter nano-KOLs; accept slower ramp — this tier buys proof, not reach.    |
| Paid waste at tiny budget                                                                                    | Retargeting only; pause <1.5x ROAS after 2 weeks.                                               |
| artists idle 14+ days · no-show <15% · artist response <4 hrs · paid cost per booking < RM 40<br>Promo abuse | One code per account; cap 100 redemptions.                                                      |

# Execute · Measure · Decide

## 30-DAY CHECKLIST

|        |                            |
|--------|----------------------------|
| Aug 10 | Confirm date + budget      |
| Sep 7  | Waitlist + RM30 offer live |
| Sep 21 | 5 wedding bloggers pitched |
| Sep 28 | 20 anchor artists (gate!)  |
| Oct 5  | DAY 0 — soft launch        |
| Oct 12 | Retargeting ON (week 2)    |

Thu.  
GA4/Meta events verified Sep 7 · referral live Oct 5 · founder batches content Mon +

## UPGRADE / DOWNGRADE

|         |                                                                                                                  |
|---------|------------------------------------------------------------------------------------------------------------------|
| Upgrade | 80% → move to Medium (RM 40k) for Q1'27 CNY season.<br>Day-60: ≥8 bookings/wk + CAC ≤ RM 15 + artist retention ≥ |
| Hold    | supply/checkout/demand before spending more.<br>Day-90 GMV/wk < RM 1,500 → diagnose                              |

## REMAINING CHECKLIST

|        |                                  |
|--------|----------------------------------|
| Nov 10 | Co-hosted pop-up                 |
| Dec 4  | Day-60 checkpoint                |
| Jan 4  | Day-90 review → upgrade decision |

# Prove it first.

Full plan: [docs/launch-marketing-plan-low.md](#) · Tiers: [docs/launch-marketing-plan-tiers.md](#)

season.

**Next step:** run the 10-item founder checklist; the Day-60 checkpoint decides whether Leish! earns the Medium budget for CNY

*#BookBeautyAnywhere · #NeverDMForADate · Your Beauty, Perfected.*

# Pick a tier. Launch Oct 5.

**Decision path:** Low proves economics → Medium grows it → High captures wedding season. Close the 7 blockers by Aug 10.

*#BookBeautyAnywhere · #NeverDMForADate · Your Beauty, Perfected.*
